



## **WATER SUPPLY EMERGENCY PROJECTS**

*Part 8, Water Regulation 2002*

Monthly Progress Reports

June 2011

Queensland Water Commission  
PO Box 15087 City East Qld 4002  
Phone: (07) 322 78207 Fax: (07) 322 78227  
Website: [www.qwc.qld.gov.au](http://www.qwc.qld.gov.au)  
ABN: 65 242 9 08 036

## 1 Background

In response to the water supply emergency in South East Queensland (SEQ), the then Minister for Water announced the making of a Regulation in 2006 to secure the water supply of the region.

The *Water Regulation 2002* (Regulation) under the *Water Act 2000* provides for a coordinated set of actions to be undertaken by State and Local Government entities.

This Regulation requires local governments and other service providers to undertake specified Measures and achieve Outcomes. Timelines for completion of the actions and target water volumes to be achieved were outlined in the Regulation.

Section 87(1)(b) and Section 88(1)(b) of the Regulation set out a requirement for all service providers to submit a progress report by the 5th working day of each month, with the reports to be published on the internet.

This report provides an overview of the performance of the regulated projects, and outlines the impact of the current progress on the overall drought strategy.

## 2 Program Overview and Drought Strategy Impacts

### Project Status

All nominated service providers submitted project reports in accordance with the Regulation.

There has been little variance against previously reported project schedules this month with most projects reporting progress in accordance with the Regulation targets.

Projects that have been previously completed:

- Brisbane Aquifer Project;
- Gold Coast to Logan transfer project;
- Cedar Grove Weir;
- Bromelton Off-Stream Storage;
- Brisbane City Council – substitute recycled water to industrial customers;
- Domestic Retrofit;
- Moreton Bay Regional Council – substitute recycled water to industrial customers;
- Southern Regional Water Pipeline;
- Eastern Pipeline Interconnector;
- Northern Pipeline Interconnector Stage 1, Ewen Maddock Water Treatment Plant;
- Enoggera Dam Water Treatment Plant Upgrade;
- Gold Coast City Council - substitute recycled water to industrial customers;
- Water Saving Initiatives – Business Water Efficiency Program; and
- Pressure and Leakage Management Project.

Furthermore, construction has been completed on the Western Corridor Recycled Water Project and is now in the commissioning or proving period phase.

The South East Queensland (Gold Coast) Desalination Project is complete and no further monthly reports are required from the service provider in relation to this project.

With the cancellation of the Traveston Crossing Dam, monthly reports are no longer required for the project. The Community Futures Taskforce ceased operation on 30 June 2010. The


Coordinator-General has now taken over responsibility for the land management and disposal of properties previously acquired by Queensland Water Infrastructure Pty Ltd for the Traveston Crossing Dam.

The *South East Queensland Water Strategy* (Strategy), released on 15 July 2010, states that additional supplies beyond existing projects will not be required until at least 2021/2022 based on demand growth. The Strategy states that, if residents can maintain an average consumption of 200 L/p/day, construction of a new source of supply may be deferred from 2021 to around 2027. The Strategy also identifies potential bulk water supply options for detailed investigation.

Issues associated with several projects are detailed in Section 3 of this Summary.

### Water Balance Impacts

During June 2011, the combined storage levels of Wivenhoe, Somerset and North Pine Dams was 88.9%. Inflows to these storages during June 2011 totalled 38 609 ML. The combined Grid 12 volume was 90.3%.

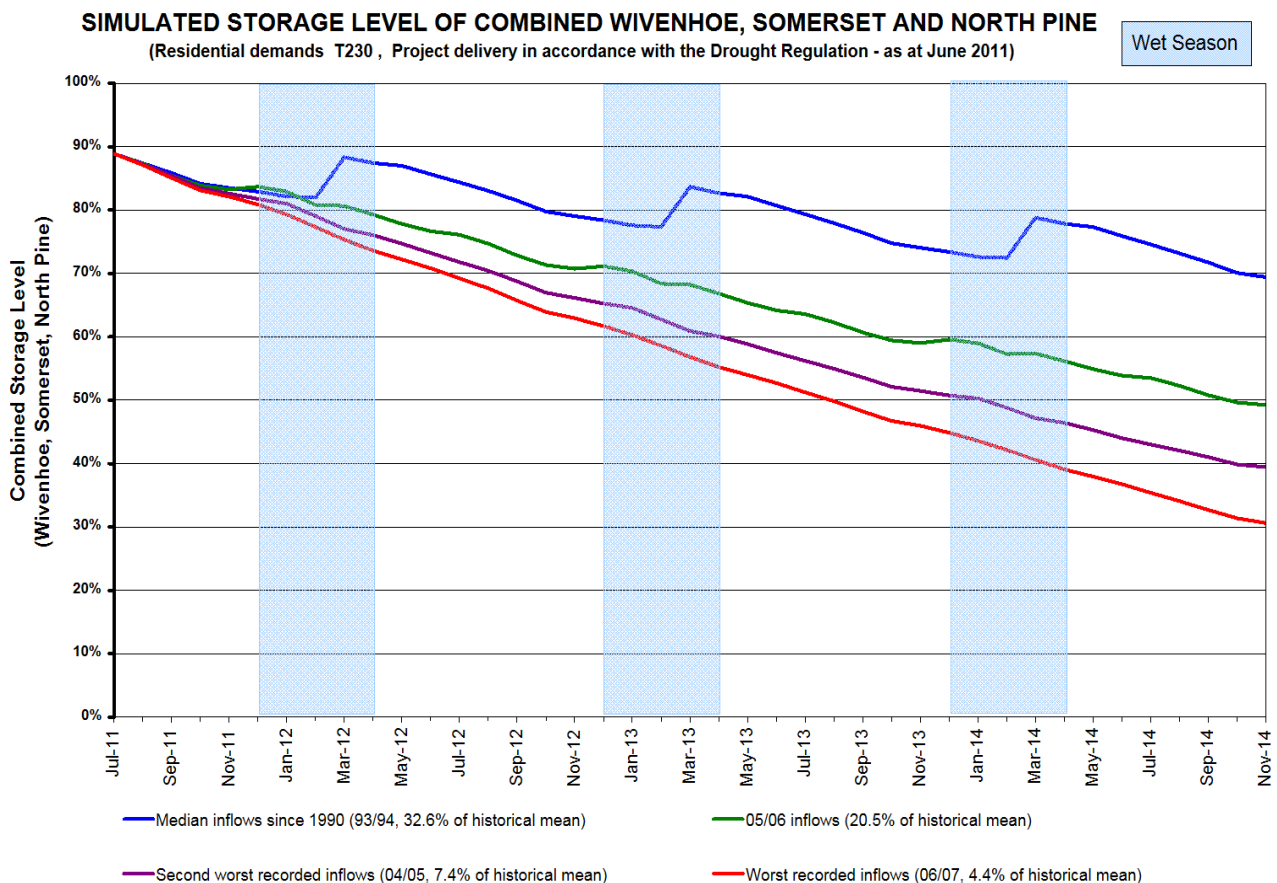

**Figure 1: Forecast Wivenhoe, Somerset and North Pine Dam storage levels based on repeated inflows**

Permanent Water Conservation Measures were introduced across SEQ on 1 December 2009, allowing people to use water efficient equipment in their gardens.

Figure 1 is modelled on the basis of an average residential consumption 230 L/p/day. On this basis, the Wivenhoe, Somerset and North Pine Dams are not forecast to fall below 40% of the combined storage capacity until April 2014 at the earliest. The modelling is based on the current instructions issued by the SEQ Water Grid Manager.

Figure 1 depicts the impact on the Wivenhoe, Somerset and North Pine Dam storage levels, considering the forecast delivery of the Regulation projects. This provides for four different dam inflow scenarios including repeated 2006/07 inflows (worst year on record); 2004/05 inflows (third worst year on record); 2005/06 inflows (as a comparison have also been analysed) and 1993/94 inflows (median inflows for the period 1990-2006).

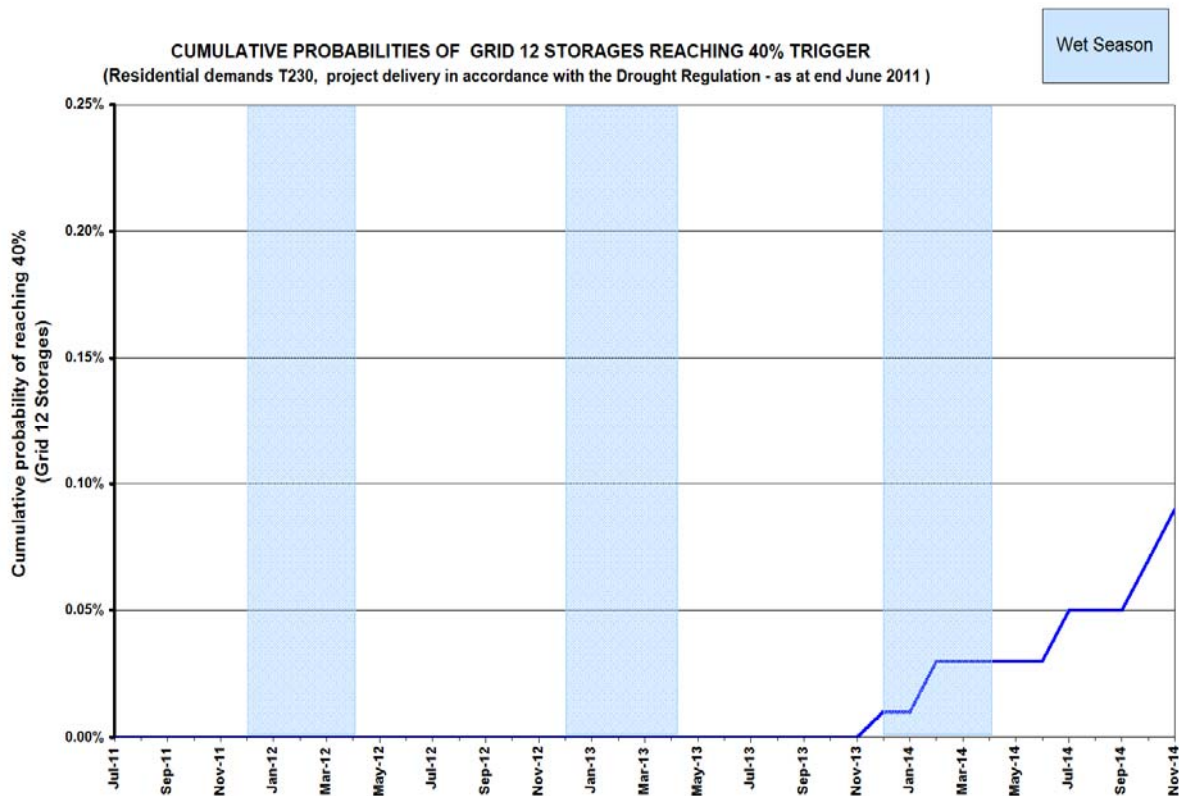


Figure 2: Forecast cumulative probability of Grid 12 storages reaching 40%

Figure 2 shows the cumulative probability of Grid Twelve storages reaching the 40% trigger at any time up to and including a particular date. For example, the probability of the Grid Twelve storages reaching 40% at any time up to and including November 2014 is less than 0.1%. The probabilities quoted are based on 100,000 years of stochastic climatic and hydrologic data generated from 117 years of historical data within the SEQ region. Modelling is based on average residential consumption across SEQ of 230 L/p/day, and includes an allowance for forecast population growth.

Both figures assume the SEQ Water Grid will be operated in accordance with the existing System Operating Plan. The System Operating Plan requires the SEQ Water Grid Manager minimise operating costs while maintaining regional water security.

Neither model provides for temporary draw down of dam levels to 75% prior to the commencement of the 2011-2012, or subsequent, wet season.

### 3 Projects Requiring Attention

Projects with challenges meeting timeframes or outcomes are discussed below:

#### Measure 1 - Bribie Island Groundwater project

*Issue:*

This Measure requires the capability to supply up to an extra 5 ML/day of water sourced from Bribie Island by 13 June 2008.

*Status:*

The Southern borefields, have supplied up to an additional 0.9 ML/day of water from November 2007. Supply from the Northern bores originally was delayed due to final approval under the *Environmental Protection and Biodiversity Conservation Act 1999* not being received from the Federal Government until 7 April 2008.

Commissioning of the northern borefields and Banksia Beach Water Treatment Plant was completed in August 2008 and this new source has the current capacity to supply up to 3.5 ML/day into the network. Extensive groundwater monitoring systems and a management plan are in place to ensure the aquifer is not compromised by saltwater intrusion.

The WTP is currently achieving variable production volumes when running, however filter performance limits the capacity.

The lamella plate and associated equipment construction is complete.

The process for commissioning started on 23 June 2011 and is continuing. Process optimisation is in progress.

#### Measure 06/07/08 – Western Corridor Recycled Water Scheme

*Issue:*

This Measure requires the construction and commissioning of Stages 1A and 2A of the Western Corridor Recycled Water Scheme to achieve 20 ML/day by 31 August 2007, an additional 46 ML/day by 30 June 2008 respectively, and Stages 2A and 2B to achieve 116 ML/day by 31 October 2008 and another 50 ML/day by 31 December 2008.

*Status:*

##### Luggage Point Advanced Water Treatment Plant

Practical Completion was achieved on 26 July 2010. The Handover Testing Period was completed in late May 2011 with handover of the asset to Veolia in mid June 2011.

##### Gibson Island Advanced Water Treatment Plant

The main plant recommenced operation in late September 2010 and the 90 day Proving Period (PP) was completed 31 December 2010.

Outstanding issues are now being finalised in order to proceed to Practical Completion.

Water produced from both the Gibson Island and Luggage Point plants meets water quality standards.

## 4 Service Provider Reports

Attached to this report are the individual monthly reports for each project, provided by the service providers responsible for delivery of the project.

It is noted the following projects are complete and no further monthly reports are required from the service providers in relation to these projects:

### Schedule 10B Projects:

Measure 2 - Brisbane Aquifer Project

Measure 3 – South East Queensland (Gold Coast) Desalination Project

Measure 4 - Southern Regional Water Pipeline

Measure 5 – Enoggera Dam Water Treatment Plan Upgrade

Measure 9 - Eastern Pipeline Inter-connector

Measure 10(a) - Northern Pipeline Inter-connector Stage 1

Measure 14 - Minimise taking of Water

- SEQWater and SunWater
- CG01 - Cedar Grove Weir
- CG02 - Bromelton Off-stream Storage

Measure 12 – Traveston Crossing Dam Stage 1

With the cancellation of the dam, monthly progress reports are no longer required for the project.

### Schedule 10C Projects:

Outcome 1 - Substitute Recycled water

- Brisbane City Council

Outcome 2 - Substitute Recycled Water

- Ipswich City Council
- Lockyer Valley Regional Council
- Logan City Council
- Redland City Council
- Scenic Rim Regional Council
- Somerset Regional Council
- Sunshine Coast Regional Council
- Moreton Bay Regional Council
- Gold Coast City Council

Outcome 6 - Alternate Supply – Logan to Gold Coast

- Logan City Council

Outcome 7 – Pressure and Leakage Management Project

Outcome 8 - Home Retrofit

Outcome 09 - Water Saving Initiatives, Business Water Efficiency Program (BWEP)
